M. A. R. 57 (Rule 116) No. D

Measurement Book

1st and final Bill.

Serial No. .....

60115

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency..... M/S KRIDL .....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Name of work :- Improvements to Road and Asphalting at pipeline Road Left side and other roads in Mallasandra ward No. 13 Shettyhalli Sub division.						
	WO :- BBMP/EE/DD/WO/147/2017-18, 21-12-2017						
	Job code :- 013-18-000017						
	A.A :- EE/DD/AS/603/17-18, 05-12-2017						
	T.S :- CE/TS/308/17-18, 08-12-2017						
	Agr :- EE/DD/AGR/147/2017-18, 24-10-2017						
	Est cost :- Rs. 50.00 Lakhs						

Scanned by CamScanner

M. A. R. 57 (Rule 116) **No. D**

Measurement Book

60116

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
3.	providing and laying precast drain cover slab of 100mm thickness in CM 1:3 including cost of all materials, labours, curing, transportation, loading, unloading etc. It is completed as per Engineer in-charge of work.						
	covered slab	1	6.00	0.90	–	5.40	
		1	4.00	0.90	–	3.60	
		1	5.00	0.90	–	4.50	
		1	8.00	0.90	–	7.20	
		1	3.00	0.90	–	2.70	
		1	8.00	0.90	–	7.20	
						30.60	m^2

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಕೆಬ್ಬಿಹಳ್ಳ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಎಸ್.ಎಂ. ಕೃಷ್ಣ ಪರಿಸರ ಭವನ, ಬೆಂಗಳೂರು.

Scanned by CamScanner

M. A. R. 57 (Rule 116) **No. D**

Measurement Book

60121

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
		2X	2X30.00	X0.15	-	18.00	
		2X	2X30.00	X0.15	-	18.00	
		2X	2X30.00	X0.15	-	18.00	
		2X	2X30.00	X0.15	-	18.00	
		2X	2X30.00	X0.15	-	18.00	
		2X	2X30.00	X0.15	-	18.00	
		2X	2X30.00	X0.15	-	18.00	
		2X	2X30.00	X0.15	-	18.00	
		2X	2X30.00	X0.15	-	18.00	

EXECUTIVE ENGINEER
Bangalore Mahanagara Palike
Dasarahalli Division, Bangalore-560057

Scanned by CamScanner

M. A. R. 57 (Rule 116) **No. D**

Measurement Book

60122

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
		1x	2x30.00	x0.15	-	9.00	
		1x	10.50	x0.15	-	1.58	
						367.88 m^2	16/01/18
		@ Rs	542.72/m^2			=>	199653=00
13.	painting two coats after filling the surface with synthetic enamel paint in approved shades on new plastered concrete surfaces, with materials, Labours it is completed as per specification.						

Dasarahalli Division, Bangalore

Scanned by CamScanner

Audited and admitted for Rs. 4975437=00
Passed by Cheque for Rs. 450234=00

MEASUREMENT BOOK

(Date	Full description, etc, of work	Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	4652032=00	3	4	5	6	7	8
					Total	=	4408595=00 4408587=00
	Design Report, Proof checking & PMC 2% amount					=	88171=00 81897=00
	KRIDL charges (10+1)% => 11%						484945=00
	Grand Total =>						Rs. 4981702 4975437=00

Accounts Superintendent — Exec. Engineer — Shantha Division

Checked

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಎಂಜಿನಿಯರರು
ಚಿಕ್ಕಬಳ್ಳಾಪುರ ಉಪವಿಭಾಗ, ಬಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಬಿಬಿಎಂಪಿ, ರಮೇಂದ್ರನಗರ, ಬೆಂಗಳೂರು.

Certificate :-
Certified that the work is satisfactorily done.

25/01/18

Scanned by CamScanner

M. A. R. 57 (Rule 116) **No. D**

Measurement Book

60124

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8

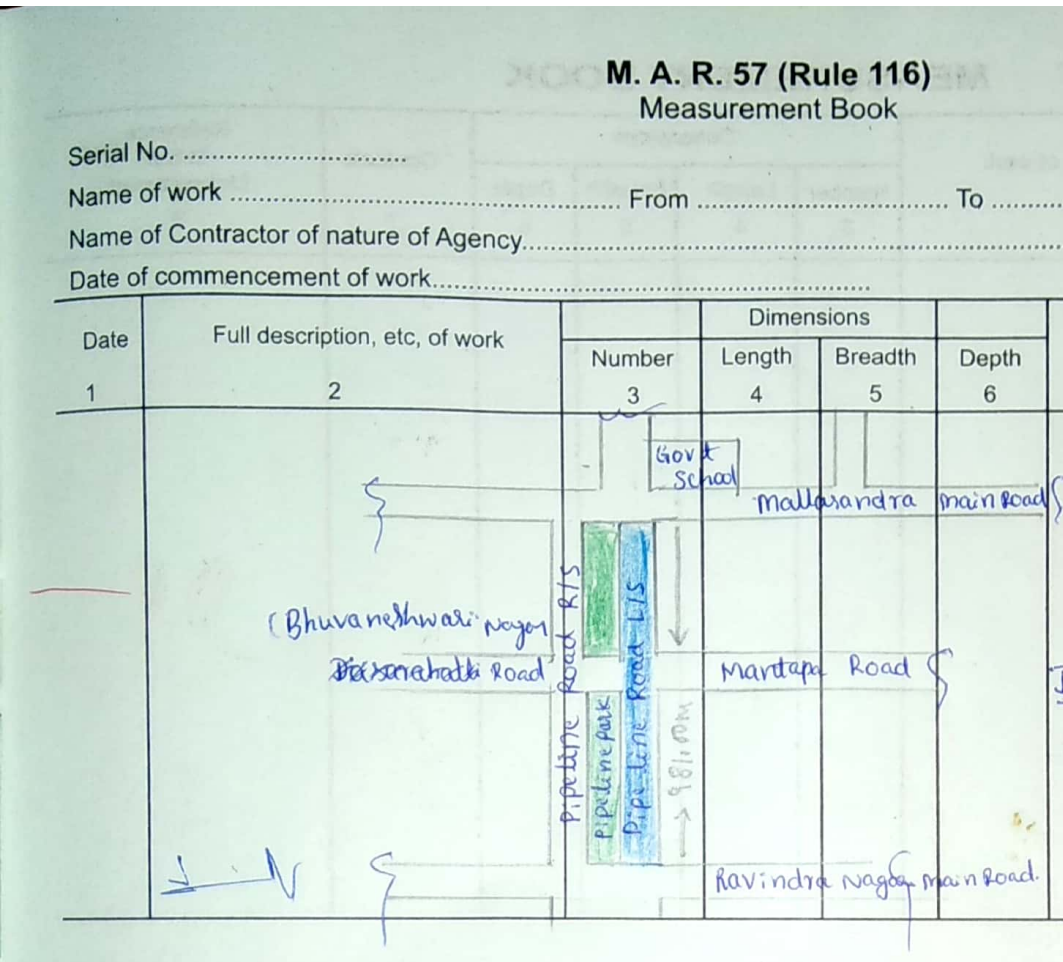

Index :-

Asphalt Road :- 981.00 m

Park :-

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರ
ಶೆಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿ

Scanned by CamScanner
